Combining TSP, CMMI, Project Management, and People Skills to Create Better Software







maintaining the data needed, and c including suggestions for reducing	lection of information is estimated to completing and reviewing the collect this burden, to Washington Headqu uld be aware that notwithstanding ar DMB control number.	ion of information. Send comments arters Services, Directorate for Infor	regarding this burden estimate mation Operations and Reports	or any other aspect of the property of the contract of the con	nis collection of information, Highway, Suite 1204, Arlington	
1. REPORT DATE APR 2010	2. REPORT TYPE			3. DATES COVERED 00-00-2010 to 00-00-2010		
4. TITLE AND SUBTITLE				5a. CONTRACT NUMBER		
Combining TSP, CMMI, Project Management, and People Skills to Create Better Software				5b. GRANT NUMBER		
Create Detter Sultware				5c. PROGRAM ELEMENT NUMBER		
6. AUTHOR(S)				5d. PROJECT NUMBER		
				5e. TASK NUMBER		
				5f. WORK UNIT NUMBER		
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) 309th Software Maintenance Group, Hil AFB, UT, 84056				8. PERFORMING ORGANIZATION REPORT NUMBER		
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)		
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)		
12. DISTRIBUTION/AVAIL Approved for publ	LABILITY STATEMENT ic release; distributi	on unlimited				
13. SUPPLEMENTARY NO Presented at the 22 City, UT.	otes and Systems and Sof	tware Technology (Conference (SSTC	C), 26-29 Apr	il 2010, Salt Lake	
14. ABSTRACT						
15. SUBJECT TERMS						
16. SECURITY CLASSIFIC	17. LIMITATION OF	18. NUMBER	19a. NAME OF			
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified	Same as Report (SAR)	OF PAGES 27	RESPONSIBLE PERSON	

Report Documentation Page

Form Approved OMB No. 0704-0188

Outline

- Purpose of the Presentation
- Historical Perspective of CMMI and TSP Alignment
- Perspective of the Presenters
- Collected Data from Eight TSP Team Leads
- Conclusions and Summary

1. Examine the assumption that TSP and CMMI are

well aligned^{1,2}.

 Share practical information (data points and opinions) from eight teams who are working in a CMMI environment to see where they think CMMI and TSP are:

2010

- Complimentary
- Conflicting



 Explore the enhancing effects of TSP on typical software project management practices.



Explore how People Skills can further enhance

TSP teams.




Historical Perspective of CMMI and TSP Alignment



2005 SEI Report

- The report titled Mapping TSP to CMMI states, "It is becoming clear that by using TSP, organizations can greatly accelerate their CMMI process improvement work." (pg. 14)
- The report also states, "there are not yet any completed studies that document the acceleration achievable in CMMI process improvement through using the TSP."^{1 (pg12)}

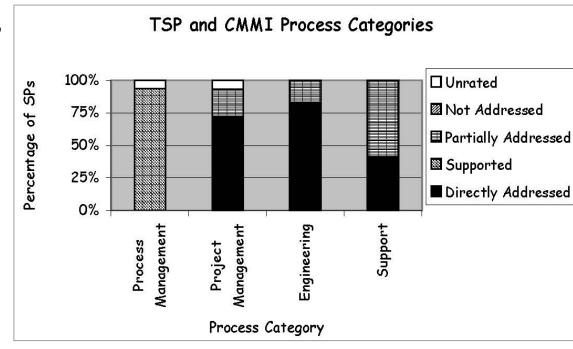

Summary of TSP Project Practice Coverage by Process Category (Source: *Mapping TSP to CMMI*, Fig 1.)

Question Posed to Watts Humphrey

• CROSSTALK: Do you see issues between the model community (CMMI) and the process community (TSP) and, if so, what are your thoughts on how to overcome such differences?

Watts' Response

"Frankly, I think in the past we have had differences, due to misunderstandings. We have been on separate paths. Fundamentally, one of the big problems they've (CMMI) got now is organizational performance with maturity. The CMMI community is beginning to see that what we've (TSP) got does work and so we are beginning to work together. CMMI and TSP are very complimentary. We are now working as a coordinated group to figure out how we can better coordinate these two approaches to help people accelerate their performance and process improvement."

- CROSSTALK May/June Issue 2010

Perspective of the Presenters



From Our Perspective

- Presenters Perspectives:
 - Technical Director and TSP Launch Coach working intricately with multiple teams and guiding groups to incorporate process and technology.
 - Project Management consultant/coach working to incorporate PMBOK best practices and to build stronger communications and team building methodologies.
 - Extended Engineering Process Group member trying to mature teams to CMMI Level 5.

Collected Data

Examining Information from Eight TSP Team Leads



1. What specific areas of CMMI and TSP work well in combination and why?

- Engineering PAs, Project Management PAs, and several Support PAs.
 - Project Planning
 - Utilization of historic data
 - Stakeholder meetings (launch meetings 1-9)
 - Team and Stakeholder Agreements (launch meeting 9)
 - Project Tracking
 - Aggregated data from individuals
 - Earned value granularity (one week segments)
 - Real-time rebalance
 - Quality Focus
 - Quality Manager (launch meeting 2)
 - Quality Plan (launch meeting 5)
 - Quality Reporting (weekly)
 - Individual quality tasks



Team Lead Quotes in Reference to Question 1.

- "The measurement PA (MA) is also greatly enhanced by TSP because the TSP teams have a common framework and experience for defining and using measures."
- "The Causal Analysis and Resolution is also a good fit with TSP because TSP teams regularly practice quantitative post mortems."

2. What areas of CMMI and TSP conflict in combination and why?

- Process Management PAs
 - CMMI defines Quantitative Project Management differently than do TSP teams.
 - Organizational Process Performance
 - Organizations usually have a mix of TSP and non-TSP teams
 - TSP tracks process as a single unit (launch to postmortem)
 - What is useful for TSP may not be for others
 - Time on task
 - Roll-up data may not match
 - Note: Although not a perfect fit, TSP teams collect enough data to make the model work, but aligning the models can be difficult.



Team Lead Quotes in Reference to Question 2.

- "CMMI has almost a top down command hierarchy assumption (e.g., the inclusion of a policy requirement in all PAs), whereas TSP is very much of a bottom up approach."
- "CMMI assumes discipline is enforced from above whereas TSP assumes that discipline is a internally driven."
- "Organizational Innovation and Development is done at a higher level in CMMI than in TSP."

3. How are project management functions (planning, scheduling, estimating, and tracking) affected by TSP disciplines?

1. Initial, robust TSP planning (launch meeting 1)

- Requirements, strategy, estimates, and schedules
 - No work until there is a concurrence from management and customers regarding the areas above.
- Weekly TSP Team meeting is real-time tracking tool
 - Schedule performance
 - Achievement of planned hours (EVM)
 - Re-evaluation of estimates
 - Workload re-balance (resource loading)
 - Risk management (probability and impact)
 - Re-planning (estimates, assignments, approval)

Team Lead Quotes in Reference to Question 3.

- "Assuming you use TSP Dashboard, it assists in re-planning when change occurs."
- "Because everyone on the team has a personal plan and collects personal data which they then share with the team, the team's weekly meeting becomes a critical real time project management tool."
- "These functions (PM) are the very core of TSP."

4. How have People Skills further enhance your TSP projects?

- TSP intensity requires a high level of communication
- Team building
 - Recognizing people (team can overshadow the individual)
 - Managing team dynamics
 - Reduce finger pointing
 - Rebalancing workload (fine balance)
 - Mentoring
- Removing barriers (political)
- Redirecting focus to quality not schedule



Team Lead Quotes in Reference to Question 4.

- "Soft skills are the most important skill a TSP leader can have."
- "Communication teams have to have a clear focus of what their management expects of them and then the team meetings need to track those goals."
- "The team leader also has to know the abilities, strengths, weaknesses, etc. of the team and manage to those as well."

Ancillary comments from the collected data?

- "A careful analysis must be done to correlate each activity dictated in CMMI and TSP. Our team created a mapping to ensure this happens, because it doesn't happen naturally."
- "Examine team dynamics; counsel, discipline and even remove those who are disrupting, abusing or ignoring other members. This is one of the most difficult soft skills, because the most disruptive people are sometimes the high performers."

Summary and Conclusion



Summary

- Many TSP practices lend themselves to CMMI PAs (Engineering, Project Management, Support)
- CMMI drives top down and TSP drives bottom up
- Conflicting areas include:
 - Organizational Process Performance
 - Aligning data and reporting
- TSP can be the answer for lacking PM practices.
 - Through TSP, PM activities occur early and often
 - PM significantly enhanced by TSP practices
- Soft skills cannot be ignored and are essential if teams want to be successful.
 - Be careful, TSP can drive soft skills out of a team because of the focus on schedule and process.

Conclusion

- Performing TSP in a CMMI environment produces the best results when the manager is focused on team dynamics and is well educated in reference to CMMI, TSP, and PM practices. The manager can then:
 - Make the correct alignments where misalignments occur
 - Obtain and utilize greater PM control
 - Manage and motivate team members for greater productivity and harmony.

Contact Information

Dave Webb 309th Software Maintenance Group david.webb@hill.af.mil (801) 586-9330



Kasey Thompson:
Software Technology Support Center kasey.thompson@hill.af.mil
(801) 586-1037





Notes

- McHale, James & Wall Daniel, Mapping TSP to CMMI, Software Engineering Institute, Pittsburgh, PA, 2005, CMU/SEI-2004-TR-014 http://www.sei.cmu.edu/reports/04tr014.pdf>
- 2. Koch, Alan S., TSP Can Be the Building Blocks for CMMI, CrossTalk, 2005

<www.stsc.hill.af.mil/crosstalk/2005/03/0503koch.html>
